

Ealing Fields High School
Summer 2018 Temporary Scheme

WE'RE
SPECIALISTS
IN FITTING OUT
AND
REFURBISHING
BUILDINGS

THE DOCUMENT:

The **Scape Construct** information evening for **Residents** affected by the **Ealing Fields 2018** scheme.

THE PROJECT:

Ealing Fields High School 2018 Temps

THE PROGRAMME:


13 Weeks

THE DEADLINE:

3rd September 2018

PROJECT OVERVIEW:

The relocation of modular buildings from Elthorne Park school to Ealing Fields School, with extensive Mechanical & Electrical Upgrades.




PROJECT DELIVERY TEAM

BUILDING GREAT SPACES

Education & Skills Funding Agency	Sharon McHale	Project Director
	Mel Speed	Project Manager
Aecom	Kevin Read	Lead Technical Advisor
	Kate Wonson	Technical Advisor
Scape Construct	Dave Shaw	Project Director
	Dan Hickman	Project Manager

18065@scapeconstruct.com



SCHEME DELIVERY

BUILDING GREAT SPACES

START ON SITE

13TH JUNE

GROUND WORK COMPLETE

5TH JULY

CRANE LIFTS AND TRANSPORTATION

6TH JULY – 16TH JULY

ELTHORNE PARK FINISHED

23RD JULY

EALING FIELDS FINISHED

27TH AUGUST

PROJECT HANDOVER

3RD SEPTEMBER



6 - 8 LORRY LOADS PER DAY

HOLDING AREAS ON SITE

SPEED LIMIT 5 MPH

NO WAITING ON PUBLIC ROADS

NO LOADS AT PEAK TIMES




FENCED OFF TURNING AREA

BANKSMAN AT ALL TIMES

SPEED LIMIT 5 MPH

ACCESS TO ALLOTMENTS

PARKING SPACES INCREASED

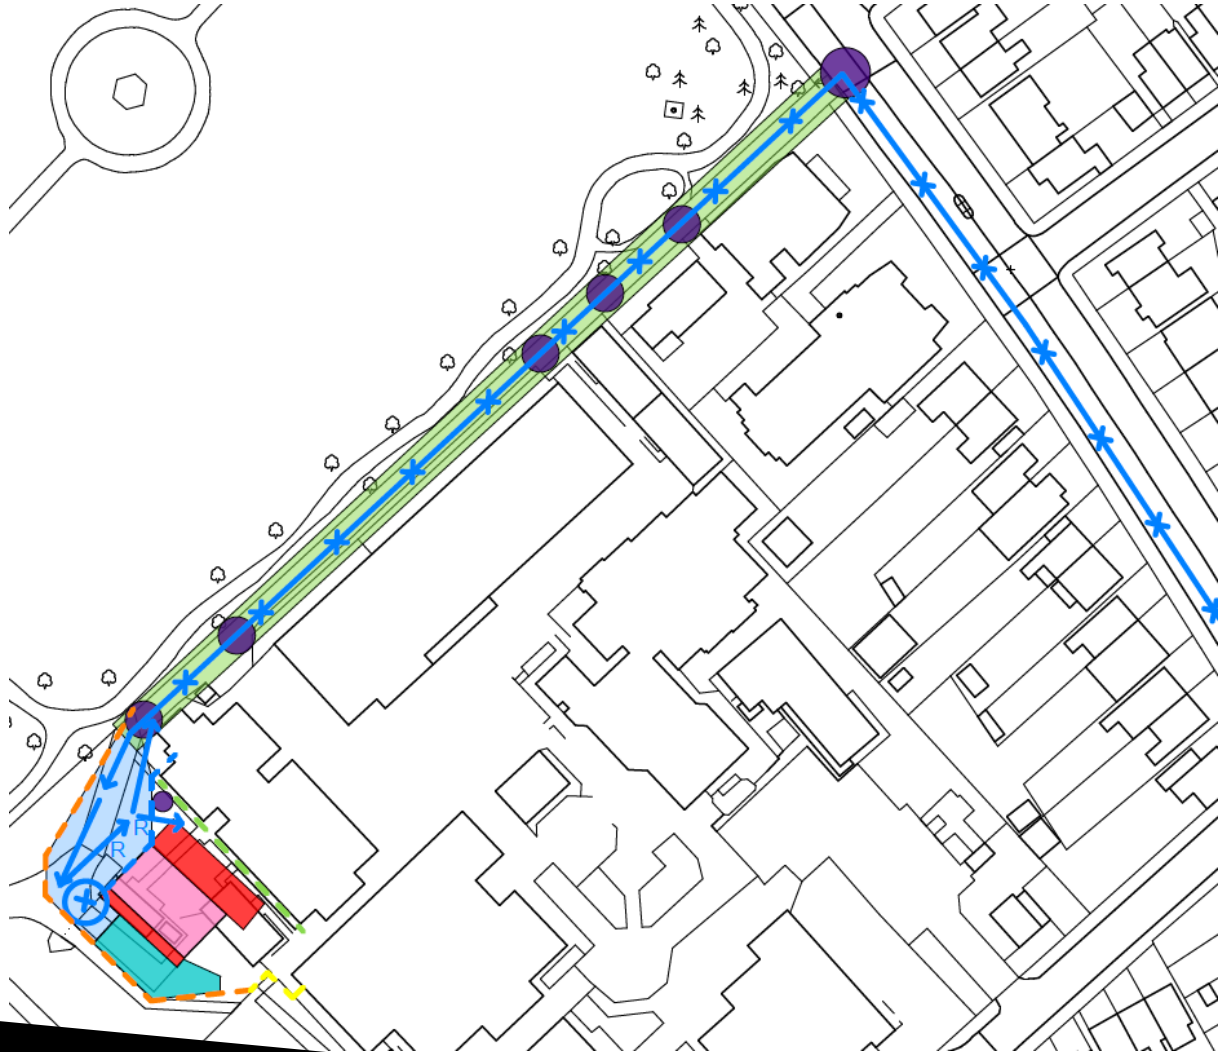

VICARAGE LANE FENCED OFF

BANKSMAN AT ALL TIMES

SPEED LIMIT 5 MPH

TREE WORK TO BE ROUTINE

NO CRANE LIFTING OVER PARK

FULLY CONTAINED SITE

REPLACEMENT OF SHRUBS

SITE HOURS

7AM – 6PM

NOISY WORKS RESTRICTED TO

9AM – 4PM

WEEKEND WORKING

NOT PROGRAMMED

CONTRACTOR PARKING

ON SITE ONLY

DUST CONTROL/CLEANING

DAILY

DELIVERY PERIODS RESTRICTED TO

10AM – 2:30PM / 4PM – 6PM

ALL HOARDING/FENCING TO BE NETTED

SIGNAGE

24/7 PROJECT TEAM CONTACT

NO UNSUPERVISED WORK

CONSIDERATE CONSTRUCTOR AUDIT

H&S AUDIT

PUBLIC INFORMATION POINTS
